

Construction Notice

July 6, 2024



Construction Update

Over the last few weeks, construction continued with sanitary sewer testing on Sandbloom Road and milling the existing HMA surface off Souwanas Trail and Oceola Drive. Additional work included grading aggregate base, parkways, and curb.

The week of July 8th the contractor will complete the cement stabilization of Souwanas Trail throughout entire project limits (weather dependent).

We are excited to have reached this project milestone and begin a critical point in construction with these roadway improvements. The map below shows the road restrictions along Souwanas Trail during that time.

- Phase 1 – July 8th
- Phase 2 – July 9th
- Phase 3 – July 10th


The project team wishes the community a safe and happy Fourth of July weekend!

The week of July 15th the contractor will begin placement of the hot mix asphalt (HMA) binder lift along the entire project limits of Souwanas.

Detour

SOUWANAS TRAIL DETOUR MAP

July 2024

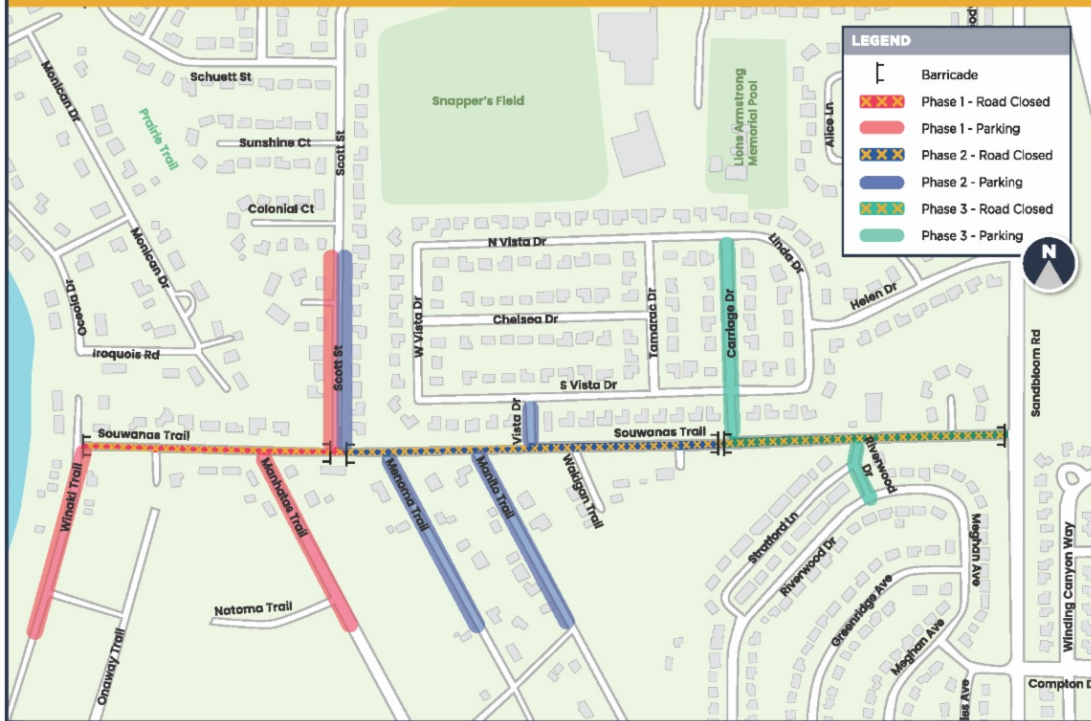

Crew milling the existing asphalt pavement at the Vista Drive and Souwanas Trail intersection.





Anticipated Project Schedule

Summer - Winter 2023

Souwanas Trail

- Install 18” sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18” sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Complete**

Schuett Street

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm sewer - **Complete**
- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

Spring - Fall 2024

- Box culvert replacement at Souwanas Creek - **Complete**
- Construct retaining wall - **Ongoing**
- Complete remaining underground improvements - **Complete**
- Curb, aprons, and sidewalk removals - **Complete**
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

Questions or concerns?

Josh Schmitt

jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road Suite 260 | Downers Grove, IL 60515
US

[Unsubscribe](#) | [Update Profile](#) | [Constant Contact Data Notice](#)



Try email marketing for free today!
