

Construction Notice

May 25, 2024



Construction Update

Over the last few weeks, the construction continued on the following items:

- Removals of existing pavement, driveways, and curb and gutter along the north limits of Souwanas Trail.
- Excavated for the proposed curb and gutter along Souwanas Trail.
- Tested the last section of the sanitary sewer improvements.
- Demobilized the equipment and material used for the sanitary sewer and water main installation from the project site.
- Installed storm sewer at the Scott Street and Souwanas Trail intersection.



After the holiday, work will continue over the next few weeks on the following items along the north limits of Souwanas Trail:

- Continue removals, excavations and aggregate subbase installation for the new curb and gutter.
- Pour the new concrete for the curb and gutter and driveways..
- Excavate and pour new concrete sidewalks.


Additional work will include:

- Preparing the south limits of Souwanas Trail for new topsoil installation.
- Removing and excavating for the proposed curb and gutter along Oceola Drive.
- Backfilling the cast in place retaining wall and installing the storm sewer.
- Adjusting the storm sewer structure to the final grade along the curbs on Souwanas Trail.

Detour

SOUWANAS TRAIL DETOUR MAP

May 2024

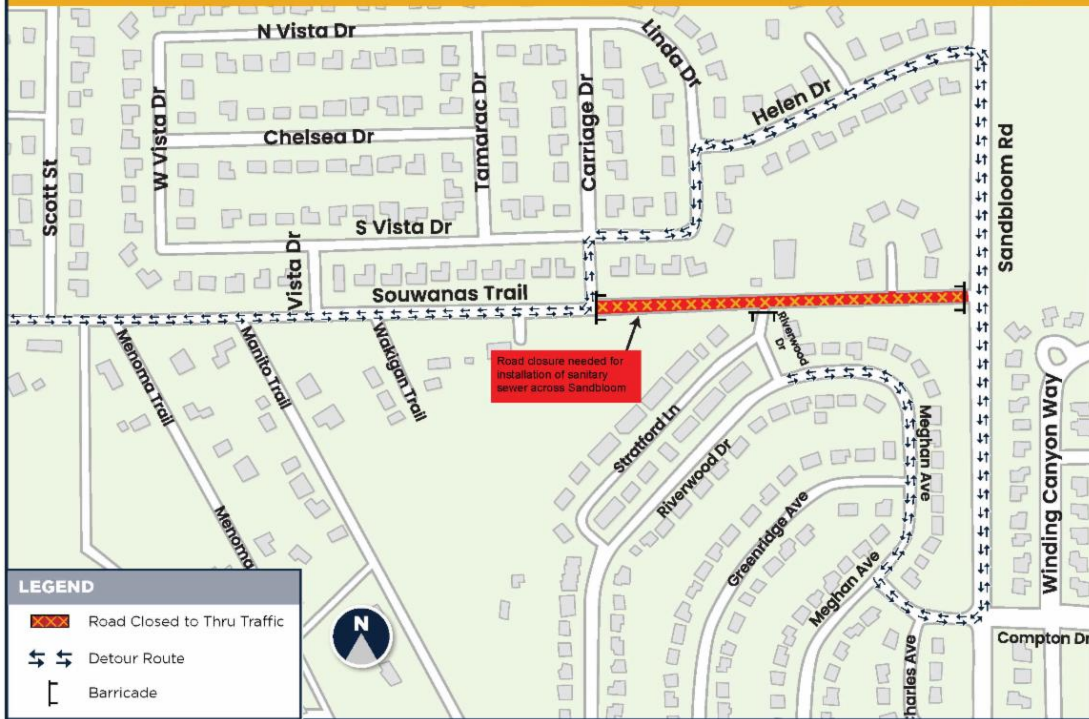

Anticipated Project Schedule

Summer - Winter
2023

Spring - Fall
2024

Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Complete**

Schuett Street

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm

- Box culvert replacement at Souwanas Creek - **Complete**
- Construct retaining wall - **Ongoing**
- Complete remaining underground improvements - **Ongoing**
- Curb, aprons, and sidewalk removals - **Ongoing**
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

sewer **Complete**

- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

Questions or concerns?

Josh Schmitt

jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road Suite 260 | Downers Grove, IL 60515
US

[Unsubscribe](#) | [Update Profile](#) | [Constant Contact Data Notice](#)



Try email marketing for free today!
