



## Construction Notice

February 17, 2024



### Construction Update

Recently, the contractor demolished the existing 48" corrugated metal pipe to make room for the proposed three-sided structure.



*Before*



*After*

#### **In the last two weeks the contractor also:**

- Temporarily decommissioned the ComEd feed at the proposed three-sided structure location
- Started excavation for the three-sided structure installation
- Placed the creek bypass into service

This week, the contractor will complete excavation and installation of an aggregate subbase for the three-sided structure. A subbase creates a stable foundation and helps distribute the weight of the three-sided structure evenly in construction. The contractor will also be mobilizing a large crane onsite that will be used to move the structure into place! The contractor be setting and placing cast-in-place concrete to complete footing and pedestal installations as well.


#### **Over the next few weeks, the contractor will:**

- Backfill the three-sided structure footings and pedestals as well as set three-sided structure archways





*During last week's excavation the contractor discovered remains of an old bridge!*

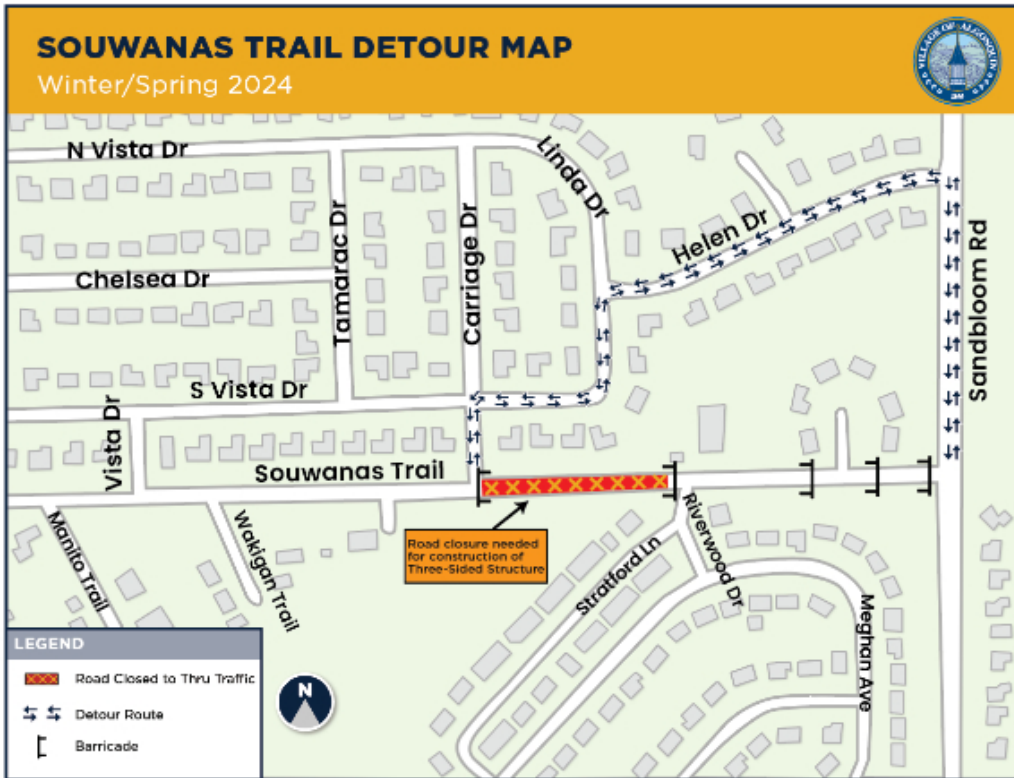

### Anticipated Project Schedule

**Summer - Winter  
2023**

**Spring - Fall  
2024**

### Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Complete**

### Schuett Street

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm sewer - **Complete**
- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

- Box culvert replacement at Souwanas Creek
- Construct retaining wall
- Complete remaining underground improvements
- Curb, aprons, and sidewalk removals
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

### Questions or concerns?

Josh Schmitt

[jschmitt@hrgreen.com](mailto:jschmitt@hrgreen.com)

[souwanasandschuettimprovementproject.org](http://souwanasandschuettimprovementproject.org)



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by



Try email marketing for free today!
