



## Construction Notice

March 30, 2024



## Construction Update

Over the next few weeks, the contractor will continue sanitary sewer and storm sewer improvements along Souwanas Trail.

### Week of April 1st

- Across Sandbloom Road

### Week of April 8th

- Riverwood Drive to Carriage Drive
- Susan Court to Riverwood Drive

The daily detour route shown below will be in place when the contractor is onsite installing the new sanitary sewer infrastructure. This typically takes place Monday through Friday between the hours of 7:00am to 4:30pm. The existing detour will remain in place at all other times, regardless of construction activities.

The contractor will also conduct pressure testing of the 10" raw water feed and connect it to Well No. 6 and the water treatment plant.

### Over the last two weeks the contractor completed the installation of the sanitary sewer in the following locations:

- The intersection of Riverwood Drive and Souwanas Trail to the intersection of Sandbloom Road and Souwanas Trail


### The contractor also completed installation of 10" raw water feed from Well No. 6 at the following locations:

- The intersection of Souwanas Trail and Sandbloom Road
- The intersection of Souwanas Trail and Riverwood Drive

### SOUWANAS TRAIL DETOUR MAP

April 2024



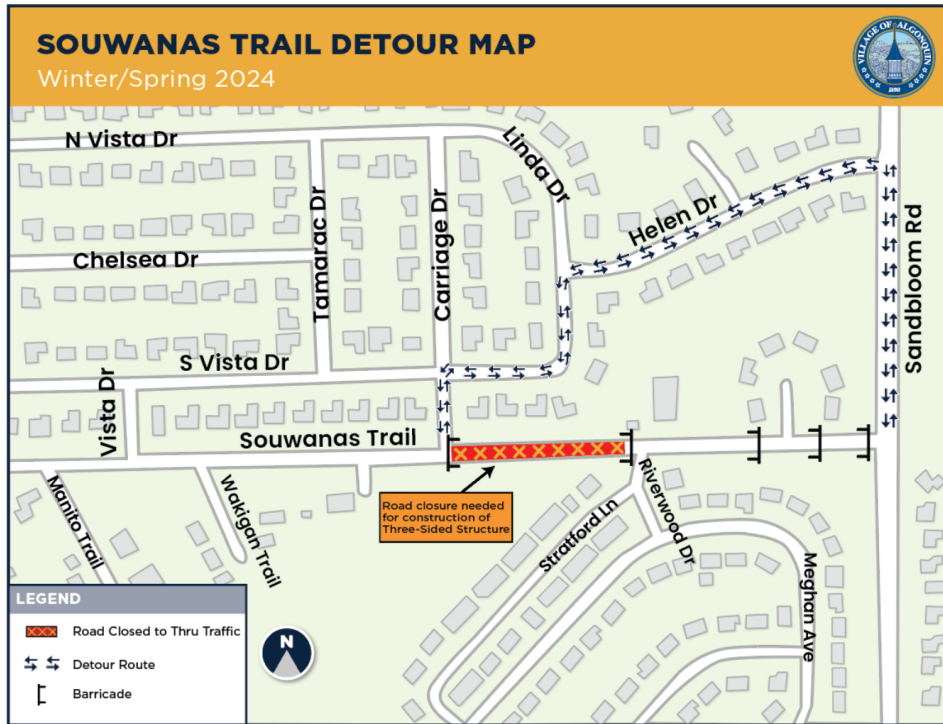

Installing the 10" raw water feed at the Riverwood Drive and Souwanas Trail

Installing the 18" raw water feed at the Riverwood Drive and Souwanas Trail intersection.



The "construction equipment train" the contractor has been using to install the 18" sanitary sewer.



## Anticipated Project Schedule

**Summer - Winter  
2023**

**Spring - Fall  
2024**

### Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Complete**

### Schuett Street

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm

- Box culvert replacement at Souwanas Creek - **Complete**
- Construct retaining wall
- Complete remaining underground improvements - **Ongoing**
- Curb, aprons, and sidewalk removals
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

sewer - **Complete**

- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

**Questions or concerns?**

Josh Schmitt

[jschmitt@hrgreen.com](mailto:jschmitt@hrgreen.com)

[souwanasandschuettimprovementproject.org](http://souwanasandschuettimprovementproject.org)



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by [twierciak@metrostratgroup.com](mailto:twierciak@metrostratgroup.com) powered by



Try email marketing for free today!
