

Construction Notice

April 13, 2024



Construction Update

Next week, the contractor will continue sanitary sewer and storm sewer improvements along Souwanas Trail from Carriage Drive to Scott Street.

The daily detour route shown below will be in place when the contractor is onsite installing the new sanitary sewer infrastructure. This typically takes place Monday through Friday between the hours of 7:00am to 4:30pm. The existing detour will remain in place at all other times, regardless of construction activities.

The contractor will also be connecting the 10" raw water feed to Well No. 6 and the water treatment plant as well as completing installation of 6" underdrains along Souwanas Trail. Excavation and installation of the cast-in-place retaining wall is also scheduled to begin. Underdrains help gather subsurface water to avoid going into the subbase of the roadway.

Over the last two weeks, the contractor completed the installation of the sanitary sewer in the following locations:


- The intersection of Riverwood Drive and Souwanas Trail to the intersection of Carriage Drive and Souwanas Trail

The contractor has also pressure tested the 10" raw water feed and installed 6" underdrains along Souwanas Trail.

Thank you for your patience as we complete the final phase of the project and please continue to drive with caution near the construction site.


SOUWANAS TRAIL DETOUR MAP

April 2024

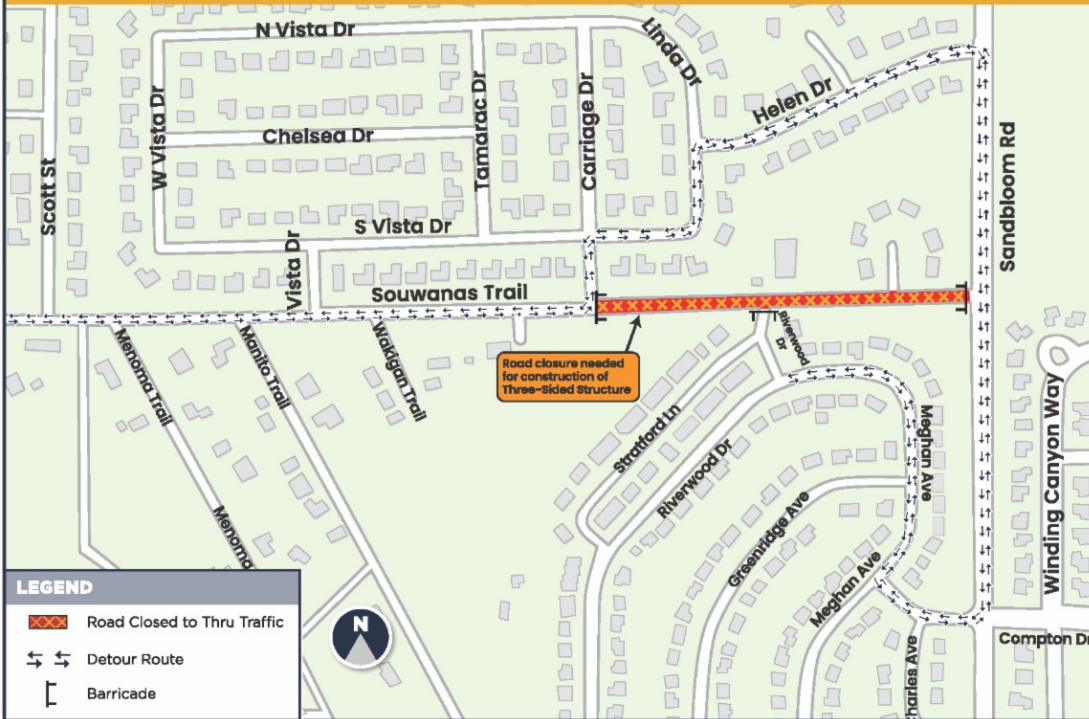

SOUWANAS TRAIL DETOUR MAP

Winter/Spring 2024

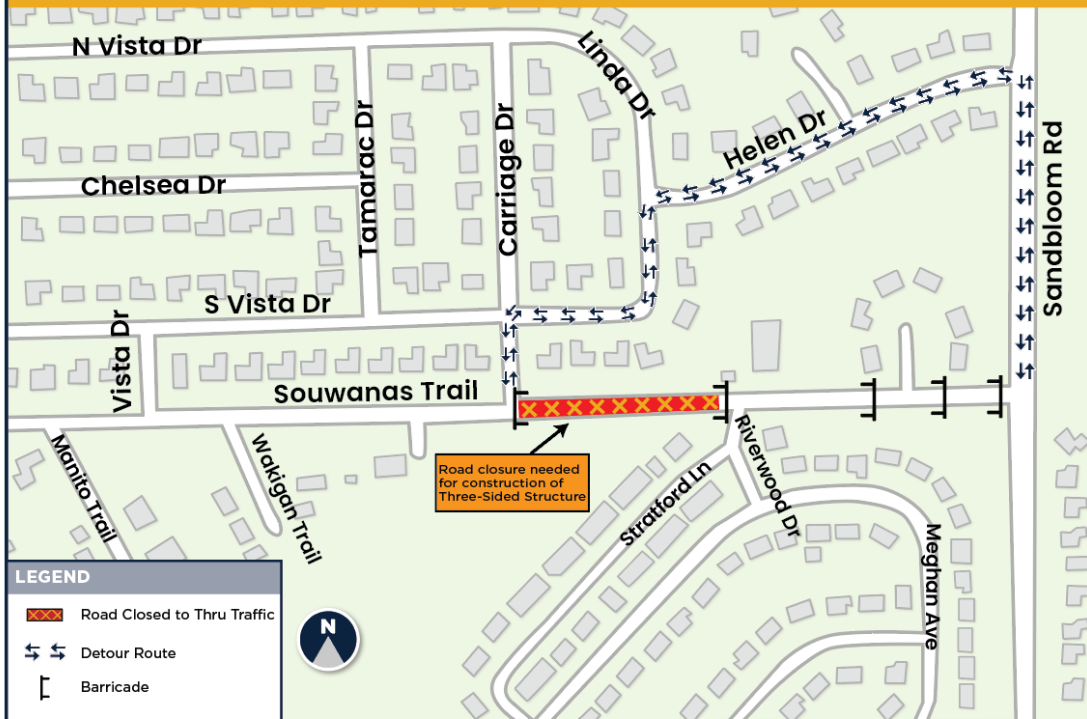



The crew installing storm sewer improvements near the intersection of Riverwood Drive and Souwanas Trail.



Anticipated Project Schedule

**Summer - Winter
2023**

**Spring - Fall
2024**

Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Complete**

Schuett Street

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm sewer - **Complete**
- Remove and replace concrete sidewalk, curb, and driveway

- Box culvert replacement at Souwanas Creek - **Complete**
- Construct retaining wall
- Complete remaining underground improvements - **Ongoing**
- Curb, aprons, and sidewalk removals
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

aprons - **Complete**

- Mill asphalt surface and begin roadway base stabilization - **Complete**

Questions or concerns?

Josh Schmitt

jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by



Try email marketing for free today!
