

Construction Notice

April 27, 2024



Construction Update

Next week, the contractor will continue storm sewer improvements at the intersection of Souwanas Trail and Scott Street with curb and gutter removal and excavation continuing along the southern limits of Souwanas Trail.

The existing detour will remain in place at all other times, regardless of construction activities.


The contractor will also begin excavation and installation of the cast-in-place retaining wall. Cast-in-place refers to concrete placed directly on a construction site instead of precast concrete, which is brought to a construction site to be assembled.

Over the last two weeks, the contractor completed the installation of the storm sewer from Wakigan Trail to Scott Street and sanitary sewer testing along Souwanas Trail from Riverwood Drive to Sandbloom Road.

The contractor has also filled the existing sewer that is no longer in use with flowable fill.

SOUWANAS TRAIL DETOUR MAP

Winter/Spring 2024

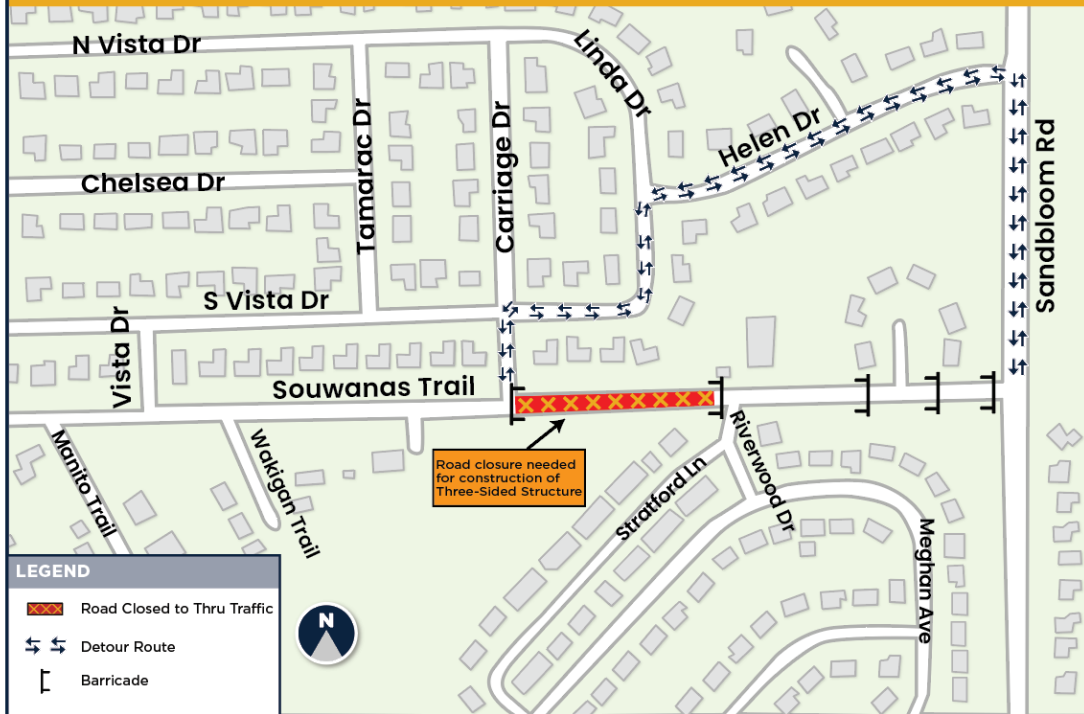

The crew installing storm sewer improvements on Souwanas Trail.



The crew installing storm sewer near the Riverwood Drive/Souwanas intersection.



Anticipated Project Schedule

Summer - Winter

Spring - Fall

2023

2024

Souwanas Trail

- Install 18” sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18” sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Complete**

Schuett Street

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm sewer - **Complete**
- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

- Box culvert replacement at Souwanas Creek - **Complete**
- Construct retaining wall
- Complete remaining underground improvements - **Ongoing**
- Curb, aprons, and sidewalk removals
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

Questions or concerns?

Josh Schmitt

jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by



Try email marketing for free today!
