

# Construction Notice

June 8, 2024



## Construction Update

Over the last few weeks, construction continued on Souwanas Trail throughout the project limits.

Along the north limits of Souwanas Trail the contractor:

- Poured concrete for new driveway aprons
- Removed existing pavement, driveway, and curb and gutter
- Installed aggregate subbase and poured concrete for new sidewalks, curb and gutter

Additional work included:

- Preparing for topsoil installation along the south limits of Souwanas Trail
- Continued storm, sanitary and water structure adjustments
- Miscellaneous overbrush grubbing



## *Crew pouring concrete for sidewalks along the north limits of Souwanas Trail*

Work will continue over the next few weeks on the following items along the north limits of Souwanas Trail:

- Removals, excavations and aggregate subbase installations for the new curb and gutter improvements
- Pouring the new concrete for the curb and gutter and driveways
- Excavating and pouring new concrete for sidewalks

Additional work will include:

- Continuing sewer infrastructure adjustments throughout the project limits
- Backfilling and installing storm sewer for the cast-in-place retaining wall

Fun fact, a cast-in-place retaining wall employs removable concrete forms to construct a vertical concrete retaining wall!




*Crew preparing the south limits of Souwanas Trail for topsoil installation*

## Detour

# SOUWANAS TRAIL DETOUR MAP

May 2024

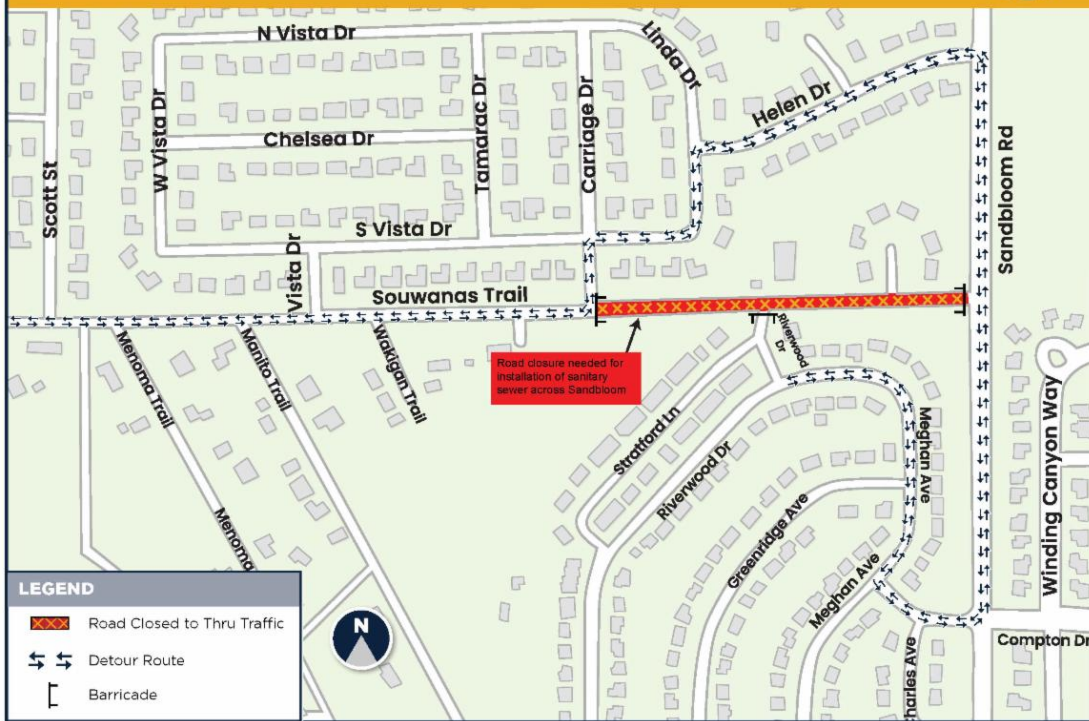

## Anticipated Project Schedule

Summer - Winter  
2023

Spring - Fall  
2024

### Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Complete**
- Box culvert replacement at Souwanas Creek - **Complete**
- Construct retaining wall - **Ongoing**
- Complete remaining underground improvements - **Ongoing**
- Curb, aprons, and sidewalk removals - **Ongoing**
- Install curb, aprons, and sidewalk

### Schuett Street

- Install new water main, new water services, and side street connections - **Complete**
- Install/upsized existing storm
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

sewer **Complete**

- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

### Questions or concerns?

Josh Schmitt

[jschmitt@hrgreen.com](mailto:jschmitt@hrgreen.com)

[souwanasandschuettimprovementproject.org](http://souwanasandschuettimprovementproject.org)



Metro Strategies Group, LLC. | 1901 Butterfield Road Suite 260 | Downers Grove, IL 60515  
US

[Unsubscribe](#) | [Update Profile](#) | [Constant Contact Data Notice](#)



Try email marketing for free today!
