

Construction Notice

June 24, 2023






Construction Update

This week, the contractor has been busy preparing the project area for construction. Work included:

- Additional traffic control material delivered to the site.
- Silt fence and inlet protection installation along Schuett Street, Souwanas Trail, and Oceola Drive.
- Equipment and material mobilization onsite for the watermain installation along Schuett Street.






SOUWANAS & SCHUETT STREETS MAP

Project Site - 2023 & 2024





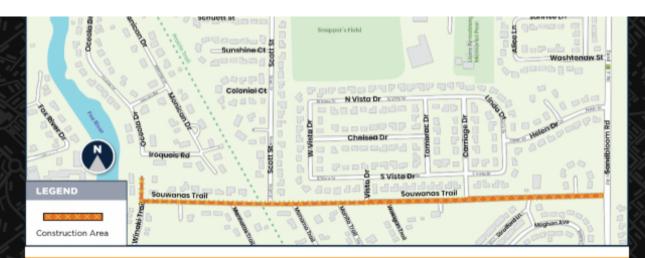







Anticipated Project Schedule

Spring-Summer 2023

Summer-Winter 2023

Spring-Fall 2024

- Private utility relocation work
- Install erosion control measures
- -Set up traffic control devices and signage
- -Set up detour route on Souwanas Trail
- -Underground improvements including deep sanitary sewer, water main, and storm sewer installation
- -Curb, sidewalk, and driveway apron replacement on Schuett Street
- -Pavement replacement on Schuett Street using the "FDR" process

- Complete remaining underground improvements
- -Pavement, curb, and sidewalk removals
- -Pavement rehabilitation work including full-depth reclamation, full-depth pavement reconstruction, curb and gutter, and sidewalk installation
- -Box culvert replacement at Souwanas Creek
- -Landscape restoration

OFRA

Questions or concerns?

Josh Schmitt jschmitt@hrgreen.com





souwanasandschuettimprovementproject.org

Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

<u>Unsubscribe twierciak@metrostrategiesinc.com</u>

<u>Update Profile | Constant Contact Data Notice</u>

Sent by twierciak@metrostratgroup.com powered by

