



Construction Notice

July 8, 2023



Construction Update

Over the last two weeks, the contractor has installed 750 feet of 8" watermain along Schuett Street from Hubbard Street to Summit Street. Nicor's contractor has also transferred gas services to the new gas main along Souwanas Trail.

Over the next two weeks, the contractor's work will include:

- Continued installation of the 8" watermain along Schuett Street.
- Installation of the 8" watermain to the side streets (Lincoln Street, Summit Street, and James Court) from the new watermain along Schuett Street.
- Installation of new fire hydrants on Schuett Street.
- Pressure connection of the 8" watermain to existing infrastructure at Schuett and Scott streets and Schuett and Hubbard streets.
- Equipment and materials mobilization for the new sanitary sewer installation along Souwanas Trail.
- Decommissioning of the old gas main along Souwanas Trail by Nicor's contractor.
- Backfill and restore the has main excavations and installation along Souwanas Trail.
- Pressure testing and chlorination of 8" watermain along Schuett Street.




- Transferring of water services to new 8" watermain along Schuett Street.
- Starting the 18" sanitary sewer installation along Souwanas Trail starting at the Oceola Drive and Souwanas Trail intersection.
- Starting the storm sewer installation along Schuett Street.

We ask all visitors, even our four legged friends, to be careful when walking near the construction site.



SOUWANAS & SCHUETT STREETS MAP

Project Site - 2023 & 2024

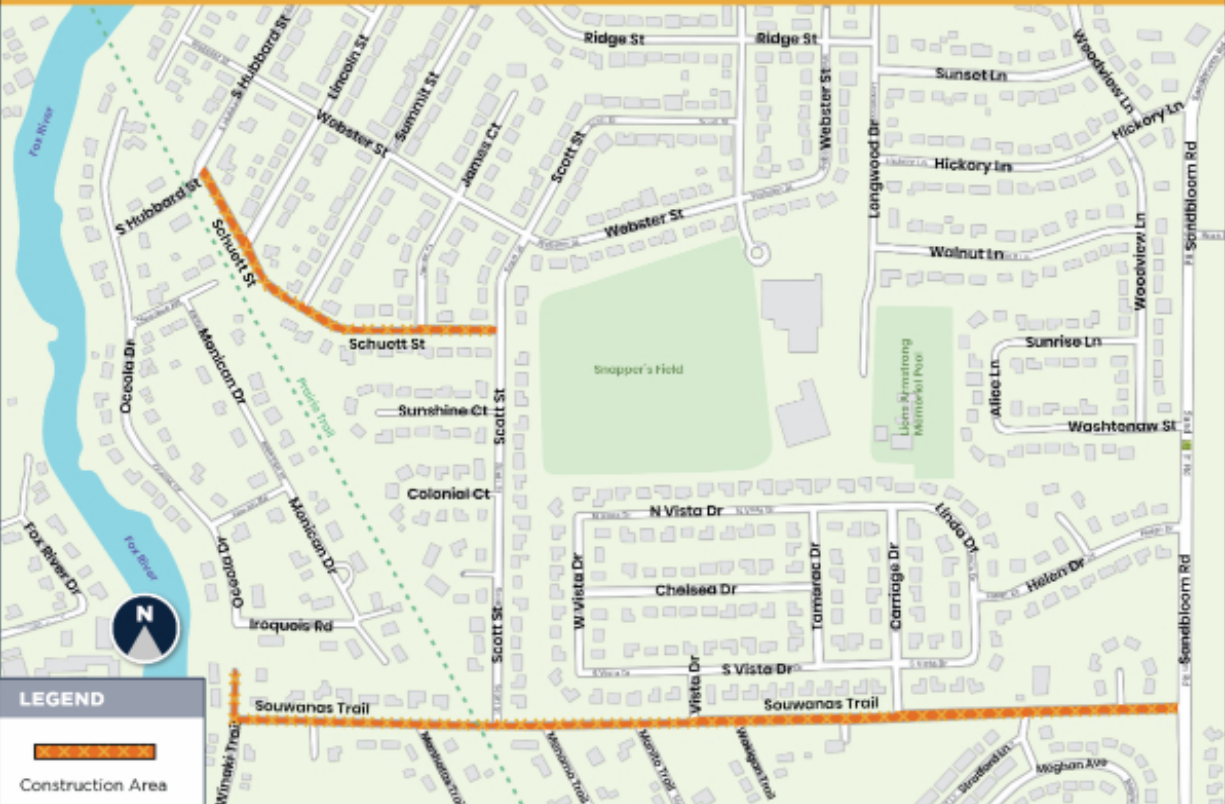

LEGEND

 Construction Area





Anticipated Project Schedule

Spring-Summer 2023

- Private utility relocation work

Summer-Winter 2023

- Install erosion control measures

-Set up traffic control devices and signage

-Set up detour route on Souwanas Trail

-Underground improvements including deep sanitary sewer, water main, and storm sewer installation

-Curb, sidewalk, and driveway apron replacement on Schuett Street

-Pavement replacement on Schuett Street using the "FDR" process

Spring-Fall 2024

- Complete remaining underground improvements

-Pavement, curb, and sidewalk removals

-Pavement rehabilitation work including full-depth reclamation, full-depth pavement reconstruction, curb and gutter, and sidewalk installation

-Box culvert replacement at Souwanas Creek

-Landscape restoration

Questions or concerns?

Josh Schmitt

jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by





Try email marketing for free today!
