



Construction Notice

August 5, 2023



Construction Update

Over the last two weeks, the underground infrastructure improvements have continued including:

- Installed the last two valve vaults (five total vaults have been installed), the last fire hydrant (four total fire hydrants have been installed) on Schuett Street.
- Connected Schuett Street water main to the existing main at Scott and Hubbard streets.
- Pressure tested, chlorinated, and placed the new 8" water main along Schuett Street into service.
- Switched over all the short side and two of the long side water service connections to the new 8" water main along Schuett Street.
- Installed the 18" sanitary sewer on Souwanas Trail from Oceola Drive to approximately Manito Trail.



Construction team preparing and completing a pressure test of the new watermain along Schuett Street.



Construction equipment train used to install 18" sanitary sewer. These two excavators work together to excavate, set the pipe, and backfill the stone after the pipe is installed.

Over the next two weeks, the contractor will complete the transfer of water services to the new water main along Schuett Street. This transfer of service


will allow the contractor to decommission the old, existing water main on Schuett Street. Additional planned work includes:

- Starting side street cross connections of new water main to existing water mains along Schuett Street.
- Pressure and vacuum testing the sanitary sewer improvements along Souwanas Trail from Oceola Drive to Manito Trail.
- Completing four pressure connections to the existing water main along Souwanas Trail and installing the associated water main.
- Continue installing 18" sanitary sewer along Souwanas Trail from Manito Trail to Vista Drive.

During the week of August 21st, the contractor will need to install a detour for Souwanas Trail to complete work. Before the detour goes into place, signage will be placed along the roadway and detour maps will be shared with residents to help provide safe alternative travel options.

SOUWANAS & SCHUETT STREETS MAP

Project Site - 2023 & 2024

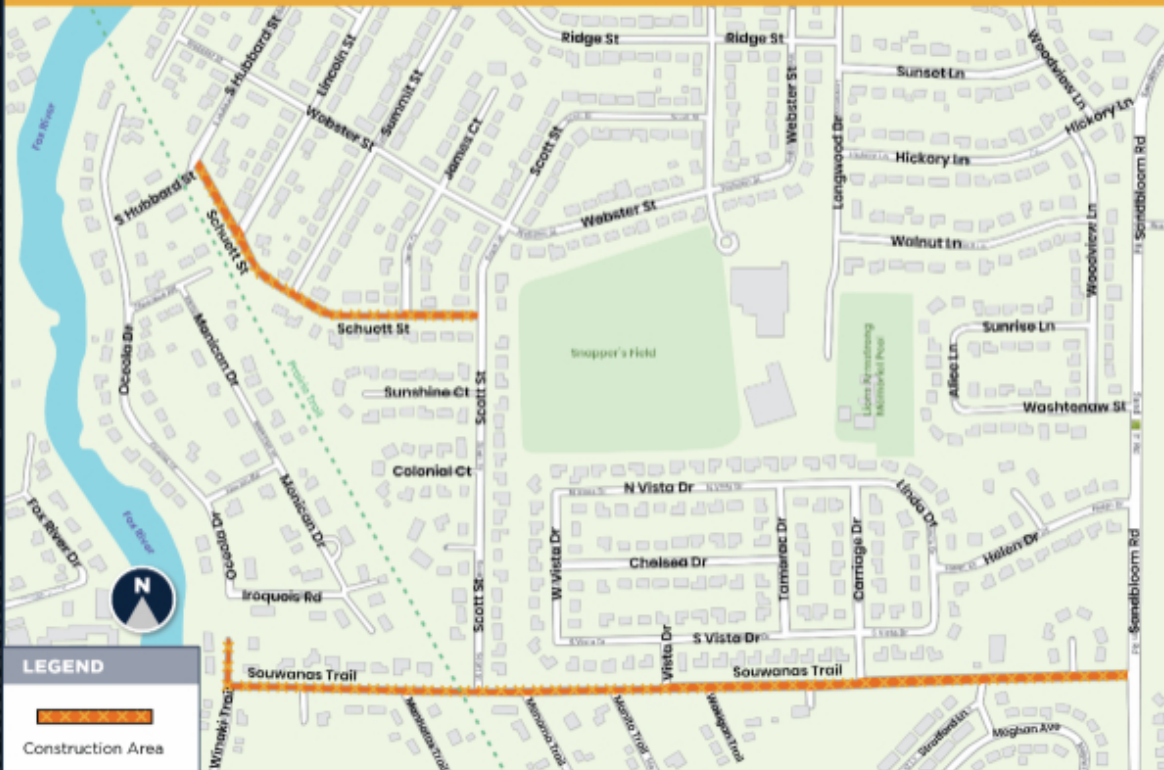

Anticipated Project Schedule

Spring-Summer
2023

Summer-Winter
2023

Spring-Fall
2024

- Private utility relocation work

- Install erosion control measures

- Complete remaining underground improvements

-Set up traffic control devices and signage

-Pavement, curb, and sidewalk removals

-Set up detour route on Souwanas Trail

-Pavement rehabilitation work including full-depth reclamation, full-depth pavement reconstruction, curb and gutter, and sidewalk installation

-Underground improvements including deep sanitary sewer, water main, and storm sewer installation

-Box culvert replacement at Souwanas Creek

-Curb, sidewalk, and driveway apron replacement on Schuett Street

-Landscape restoration

-Pavement replacement on Schuett Street using the "FDR" process

Questions or concerns?

Josh Schmitt

jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by



Try email marketing for free today!
