



Construction Notice


October 21, 2023



Construction Update

Over the last two weeks, progress has continued on the project as weather permitted. Construction has included:

- Removed the earth retention system for the jack and bore pit #2 and the pit was backfilled
- Removed and replaced the concrete curb and gutter and driveway aprons along the south side of Schuett Street
- Completed the excavation and set up of earth retention system for jack and bore pit #3
- Excavated and set up earth retention system for jack and bore pit #4 (4 total pits will be used for this project)
- Set up boring pit equipment and begin installation of 36" casing for the sanitary sewer from jack and bore pit #3

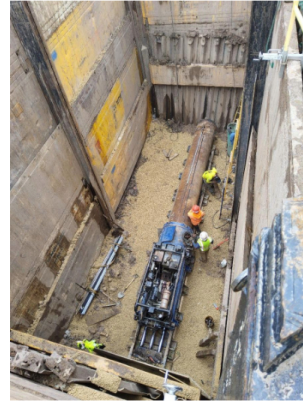

Over the next few weeks, the contractor will:

- Complete all remaining concrete work (sidewalks) along Schuett Street.
- Begin landscape restoration along Schuett Street
- Complete sanitary sewer installation at the intersection Vista Drive and Souwanas Trail
- Continue installation of 36" casing and 18" sanitary sewer from jack and bore pit #3
- Begin mainline pavement removal along Schuett Street
- Resume sanitary sewer service and sanitary main lateral installation along Souwanas Trail from Ocoola Drive to Vista Drive
- Perform cement Stabilization of existing base along Schuett Street



SOUWANAS TRAIL DETOUR MAP

September 2023





Anticipated Project Schedule

Summer - Winter 2023

Spring - Fall 2024

Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Ongoing**
- Temporary pavement

- Box culvert replacement at Souwanas Creek
- Construct retaining wall
- Complete remaining underground improvements
- Curb, aprons, and sidewalk removals
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

Schuett Street

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm sewer - **Complete**
- Remove and replace concrete sidewalk, curb, and driveway aprons - **Ongoing**
- Mill asphalt surface and begin roadway base stabilization

Questions or concerns?

Josh Schmitt
jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:unsubscribe.twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by



Try email marketing for free today!
