



## Construction Notice

February 3, 2024



### Construction Update



*10" watermain installation along Souwanas Trail*

Happy New Year! The contractor has been back at work following the holiday season. In the last two weeks the contractor has:

- Begun installation of 10" watermain along Souwanas Trail from Riverwood Drive to Sandbloom Road.
- Installed 12" storm sewer improvements and associated storm structures along Souwanas Trail from Riverwood Drive to Carriage Drive.
- Coordinated with ComEd in preparation for temporary utility removal above the proposed three-sided structure location.

#### **Next week Monday February 5th - Wednesday February 7th**


The contractor will install 10" watermain along Sandbloom Road from Souwanas Trail to Well No. 6. During this installation and while construction is occurring onsite, Sandbloom Road will be reduced to one lane from Helen Drive to Souwanas Trail. The Contractor will have flaggers onsite to direct traffic along Sandbloom Road.

#### **Over the next weeks the contractor will:**

- Install 10" watermain near Souwanas Trail and Riverwood Drive intersection.
- Prepare creek bypass pumping equipment and material for three-sided structure installation.
- Place creek bypass pumping equipment into service
- Begin excavation and required demolition for three-sided structure installation.
- Receive delivery of three-sided structure footing material.



12" storm sewer installation near the Souwanas Trail and Carriage Drive intersection

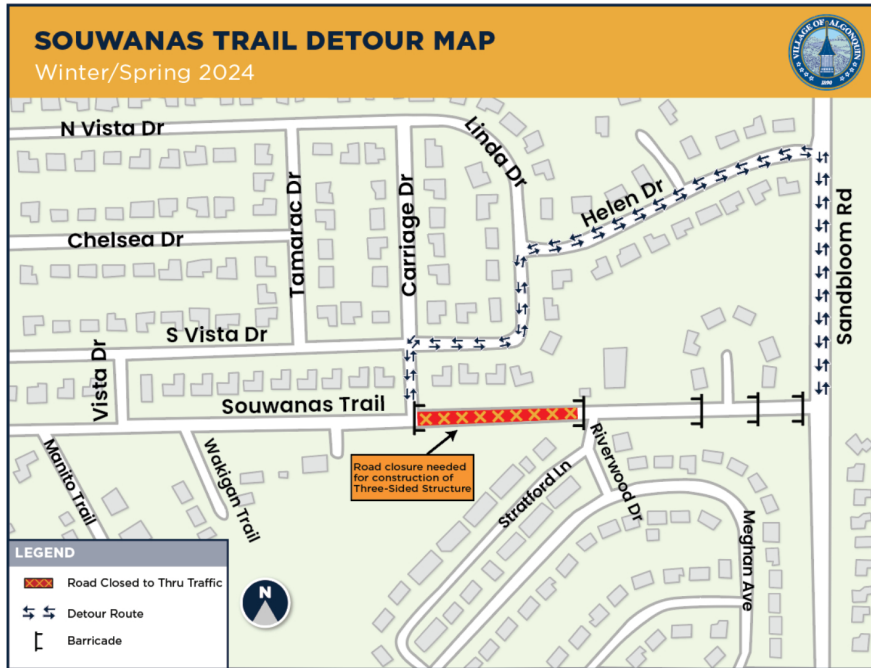

### Anticipated Project Schedule

Summer - Winter  
2023

Spring - Fall  
2024

#### Souwanas Trail

- Install 18" sanitary sewer from
- Box culvert replacement at

Oceola Drive to Vista Drive -

**Complete**

- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Complete**

**Schuett Street**

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm sewer - **Complete**
- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

Souwanas Creek

- Construct retaining wall
- Complete remaining underground improvements
- Curb, aprons, and sidewalk removals
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

**Questions or concerns?**

Josh Schmitt

[jschmitt@hrgreen.com](mailto:jschmitt@hrgreen.com)

[souwanasandschuettimprovementproject.org](http://souwanasandschuettimprovementproject.org)



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by [twierciak@metrostratgroup.com](mailto:twierciak@metrostratgroup.com) powered by



Try email marketing for free today!
