



Construction Notice

July 22, 2023



Construction Update

Over the last two weeks, the contractor has made significant progress on the Souwanas Trail and Schuett Street project.

Work completed on the project includes:

- Installed 1,000 feet of 8" watermain infrastructure on Schuett Street, from Summit Street to Scott Street (and side streets).
- Completed watermain pressure connections at Schuett and Hubbard streets and Schuett and Scott streets.
- Decommissioned old gas main lines along Souwanas Trail (NPL completed for Nicor).
- Mobilized equipment and material onsite for the new sanitary sewer installation along Souwanas Trail and began the sanitary sewer installation of 18" sewer infrastructure starting at the Souwanas Trail and Oceola Drive intersection.
- Installed two fire hydrants along Schuett Street, please note that fire hydrants are concealed within a bag to alert the fire department that it is not in service yet.



Fire Hydrant Installation






Excavation for the 18" sanitary sewer infrastructure.
(Souwanas Trail & Oceola Drive intersection.)

Over the next two weeks, the contractor will continue the installation of the 8" watermain pipe along Schuett Street. They will pressure test and chlorinate the new watermain pipe and then transfer water services to the new 8" watermain on Schuett Street. Sanitary sewer installation will continue along Souwanas Trail from Oceola Drive to Manhatas Trail and then along Souwanas Trail from Manhatas Trail to Menoma Trail. The contractor will also install the two remaining fire hydrants along Schuett Street and begin decommissioning the old watermain along Schuett Street.

SOUWANAS & SCHUETT STREETS MAP

Project Site - 2023 & 2024

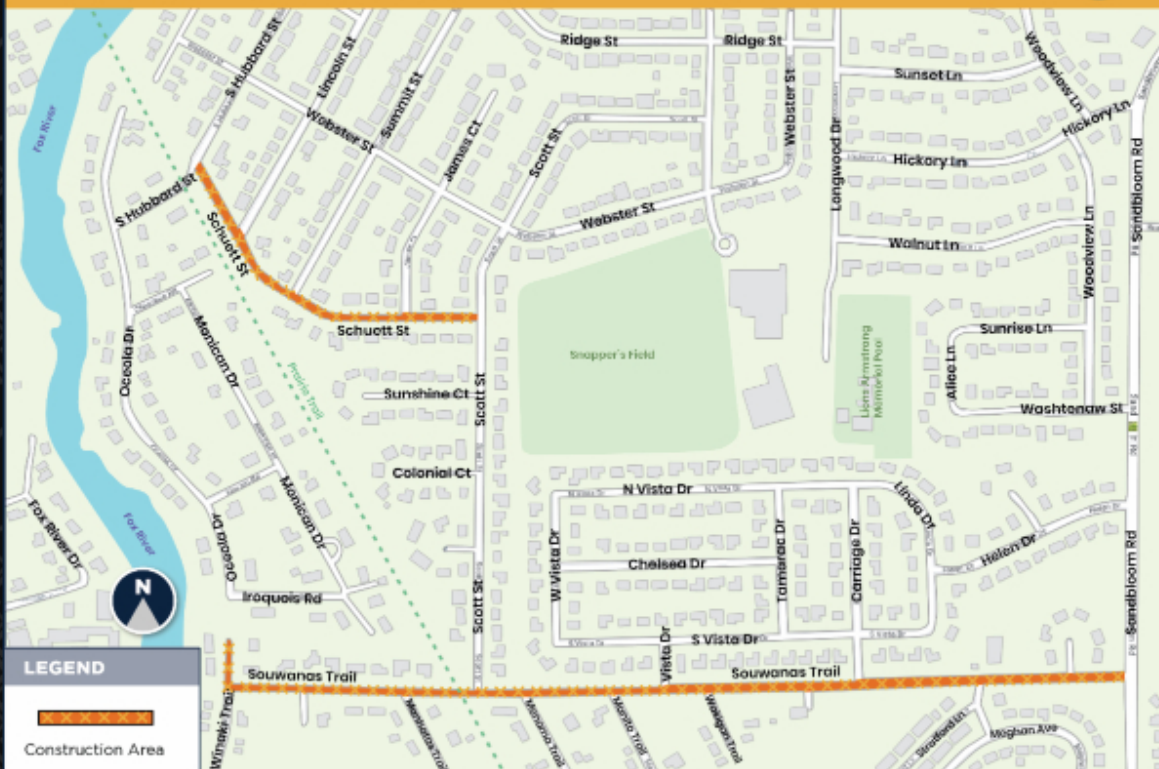

Anticipated Project Schedule

Spring-Summer
2023

Summer-Winter
2023

Spring-Fall
2024

- Private utility relocation work

- Install erosion control measures

- Complete remaining underground improvements

-Set up traffic control devices and signage

-Pavement, curb, and sidewalk removals

-Set up detour route on Souwanas Trail

-Pavement rehabilitation work including full-depth reclamation, full-depth pavement reconstruction, curb and gutter, and sidewalk installation

-Underground improvements including deep sanitary sewer, water main, and storm sewer installation

-Box culvert replacement at Souwanas Creek

-Curb, sidewalk, and driveway apron replacement on Schuett Street

-Landscape restoration

-Pavement replacement on Schuett Street using the "FDR" process

Questions or concerns?

Josh Schmitt

jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by



Try email marketing for free today!
