



## Construction Notice

September 2, 2023



### Construction Update

The Souwanas Trail and Schuett Street project continues to advance forward as we move into fall. Over the last two weeks, the contractor has:

- Completed installation (7 of 7) of the long water services along Souwanas Trail
- Pressure tested (4 of 4) water main laterals installed across Souwanas Trail
- Mobilized equipment and begin preparation of the 36" casing jack and bore installation
- Began installation of storm sewer along Souwanas Trail (starting at the intersection of Oceola Drive/Souwanas Trail)
- Performed vacuum testing of the sanitary sewer improvements installed along Souwanas Trail from Oceola Trail to Manito Trail




Over the next two weeks, the contractor has scheduled the following work:

- Begin installation of 36" casing for sanitary sewer from jack and bore pit
- Continue installation of storm sewer along Schuett Street (from the intersection of Lincoln/Schuett streets to Summit/Schuett streets)
- Lowering water main at Oceola Street/Souwanas Trail intersection
- Set up temporary sanitary sewer bypass piping for jack and bore receiving pit
- Abandonment of existing sanitary sewer along Souwanas Trail (Oceola to Vista drives)

### SOUWANAS TRAIL DETOUR MAP

August 2023

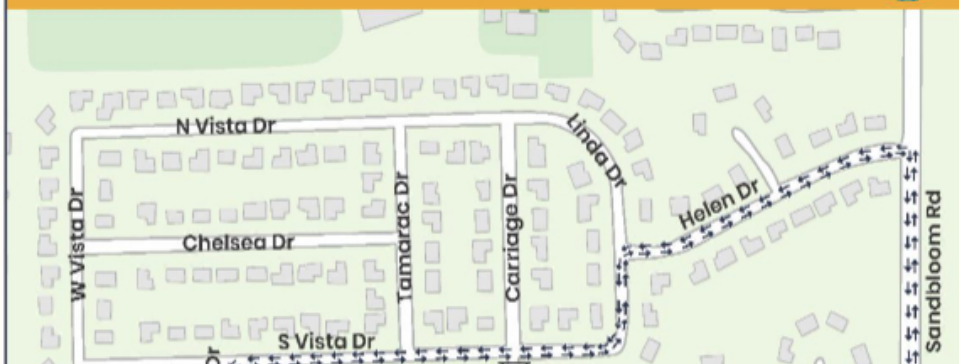



## Anticipated Project Schedule

### Spring-Summer 2023

- Private utility relocation work - **Complete**

### Summer-Winter 2023

#### Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive via open cut trench - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road
- Construct bore pits/jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek
- Install storm sewer from Oceola Drive to Scott Street

#### Schuett Street

- Install new water main, new water services, and side street connections - **Complete**
- Install/upsized existing storm sewer
- Remove and replace concrete sidewalk, curb, and driveway aprons
- Mill asphalt surface and begin roadway base stabilization

### Spring-Fall 2024

#### Souwanas Trail

- Install mainline sanitary sewer and connections
- Remove and replace three-sided box culvert
- Remove and replace concrete curb, sidewalk, and driveway aprons
- Construct retaining wall
- Mill asphalt surface, perform base stabilization and pave new asphalt surface.
- Landscape restoration and pavement markings

#### Schuett Street

- Roadway improvement work including paving new asphalt surface
- Landscape restoration

**Questions or concerns?**

Josh Schmitt

[jschmitt@hrgreen.com](mailto:jschmitt@hrgreen.com)

[souwanasandschuettimprovementproject.org](http://souwanasandschuettimprovementproject.org)



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by [twierciak@metrostratgroup.com](mailto:twierciak@metrostratgroup.com) powered by



Try email marketing for free today!
