



Construction Notice

November 18, 2023



Construction Update

The contractor has reached a major milestone with the placement of Hot Mix Asphalt (HMA) binder and surface along Schuett Street. The only work remaining on Schuett Street will be final restoration items that will be completed in the spring of 2024. Over the last two weeks, additional the construction has included:

- Placement of topsoil and temporary erosion control blanket along Schuett Street.
- Completed testing of sanitary sewer improvements from manhole 232 to 114
- Continued installation of storm sewer improvements along Souwanas Trail from Onaway Trail to Manhatas Trail
- Installed sanitary manhole 116, removed earth retention, and backfilled jack and bore pit #3
- Performed structure adjustments along Schuett Street
- Placed temporary HMA patching over storm sewer utility along Souwanas trail
- Removed trees along Souwanas Trail

As weather permits, over the next few weeks, the contractor will:


- Continue installation of storm sewer improvements along Souwanas Trail from Onaway Trail to Scott Street
- Install sanitary sewer manhole 116A and connect existing forcemain to new sanitary sewer improvements
- Place temporary erosion control blanket along Souwanas Trail
- Complete temporary HMA patching along Souwanas Trail from Oceola Drive to Carriage Drive



Erosion Control Blanket Along Schuett Street



HMA Surface Along Schuett Street

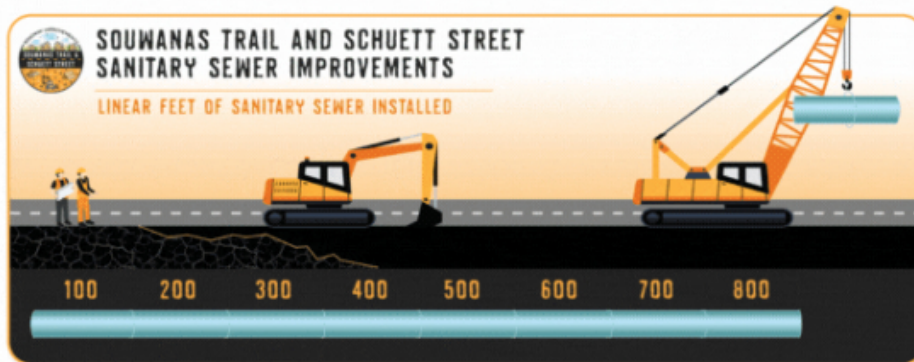

A major component of this project has been the upsizing and extension of the sanitary sewer. This project provides service to over 6,000 residents and dozens of businesses. Once complete, the project will have installed 4,000 linear feet of sanitary sewer infrastructure infrastructure with approximately 900 linear feet at depths of 30 feet!

SOUWANAS TRAIL DETOUR MAP

October 2023





Anticipated Project Schedule

Summer - Winter 2023

Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Ongoing**

Schuett Street

- Install new water main, new water services, and side street connections - **Complete**
- Install/upsized existing storm sewer - **Complete**
- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

Spring - Fall 2024

- Box culvert replacement at Souwanas Creek
- Construct retaining wall
- Complete remaining underground improvements
- Curb, aprons, and sidewalk removals
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

Questions or concerns?

Josh Schmitt

jschmitt@hrgreen.com

souwanasandschuettimprovementproject.org



[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by



Try email marketing for free today!
