



## Construction Notice

December 2, 2023



## Construction Update

The contractor achieved another major milestone and completed the installation of storm sewer improvements along Souwanas Trail from Oceola Drive to Manhatas Trail! Over the last two weeks, additional work has included:

- Installation of topsoil and temporary erosion control blanket along Schuett Street.
- Installation of temporary erosion control blanket along Souwanas Trail.
- Connecting the existing sanitary forcemain to the new improvements.
- Placement of temporary HMA patching along Souwanas Trail.

As weather permits, over the next few weeks, the contractor will:

- Complete temporary HMA patching along Souwanas Trail.
- Set up the creek bypass and install additional sanitary sewer runs and manholes.
- Install rear yard storm sewer along Souwanas Trail.
- Begin preparation for the three-sided box culvert structure installation.




*Temporary HMA placement on Souwanas Trail*






*Storm sewer installation on Souwanas Trail*



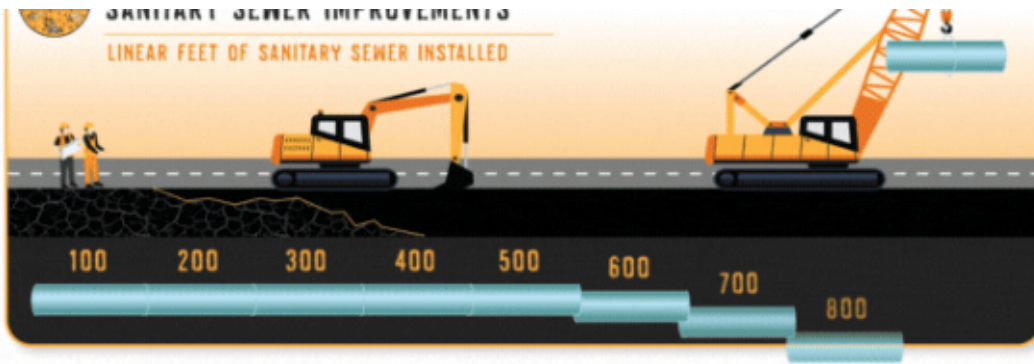

A major component of this project has been the upsizing and extension of the sanitary sewer. This project provides service to over 6,000 residents and dozens of businesses. Once complete, the project will have installed 4,000 linear feet of sanitary sewer infrastructure with approximately 900 linear feet at depths of 30 feet!

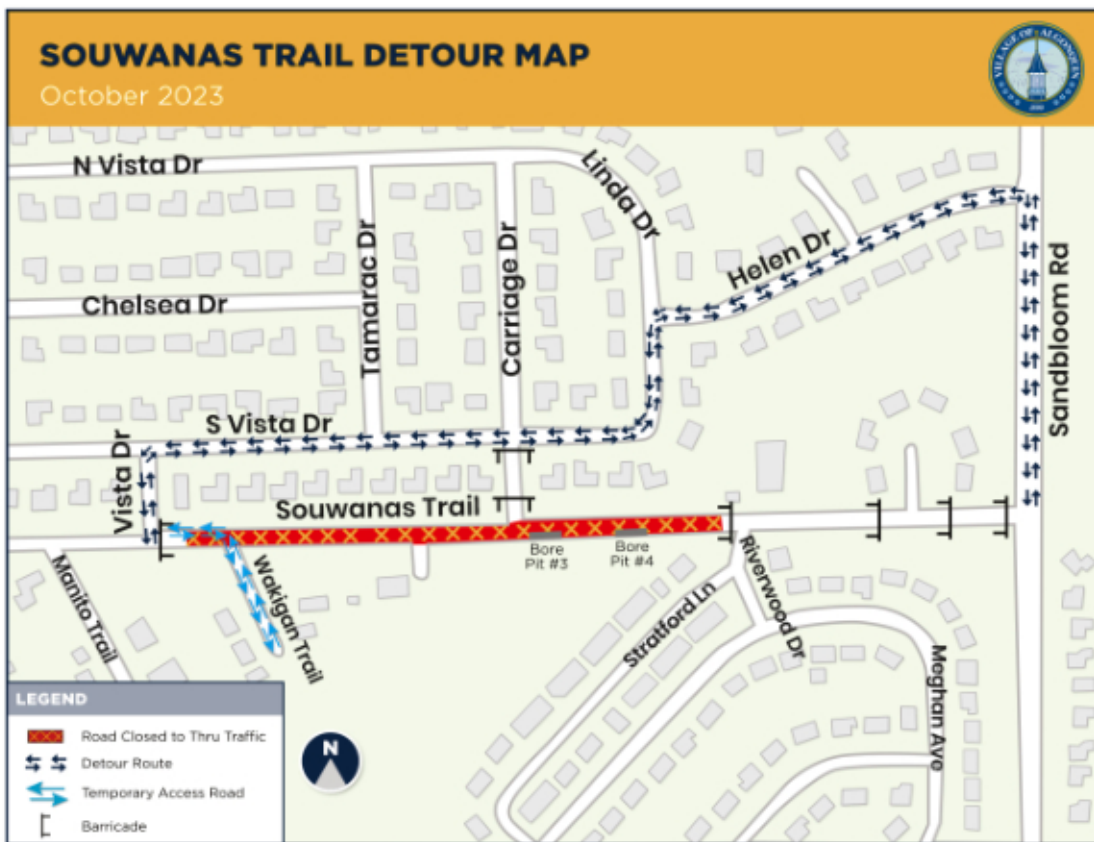

### Anticipated Project Schedule

Summer - Winter  
2023

Spring - Fall  
2024

### Souwanas Trail

- Install 18" sanitary sewer from Oceola Drive to Vista Drive - **Complete**
- Set up detour route on Souwanas Trail from Vista Drive to Riverwood Road - **Complete**
- Jack and bore deep 18" sanitary sewer from Vista Drive to Souwanas Creek - **Complete**
- Temporary pavement - **Ongoing**
- Box culvert replacement at Souwanas Creek
- Construct retaining wall
- Complete remaining underground improvements
- Curb, aprons, and sidewalk removals
- Install curb, aprons, and sidewalk
- Pavement rehabilitation: full-depth reclamation and asphalt resurfacing
- Landscape restoration

### Schuett Street

- Install new water main, new water services, and side street connections – **Complete**
- Install/upsized existing storm sewer - **Complete**
- Remove and replace concrete sidewalk, curb, and driveway aprons - **Complete**
- Mill asphalt surface and begin roadway base stabilization - **Complete**

### Questions or concerns?

Josh Schmitt

[jschmitt@hrgreen.com](mailto:jschmitt@hrgreen.com)

[souwanasandschuettimprovementproject.org](http://souwanasandschuettimprovementproject.org)



Metro Strategies Group, LLC. | 1901 Butterfield Road, Suite 260, Downers Grove, IL 60515

[Unsubscribe twierciak@metrostrategiesinc.com](mailto:twierciak@metrostrategiesinc.com)

[Update Profile](#) | [Constant Contact Data Notice](#)

Sent by twierciak@metrostratgroup.com powered by



Try email marketing for free today!
